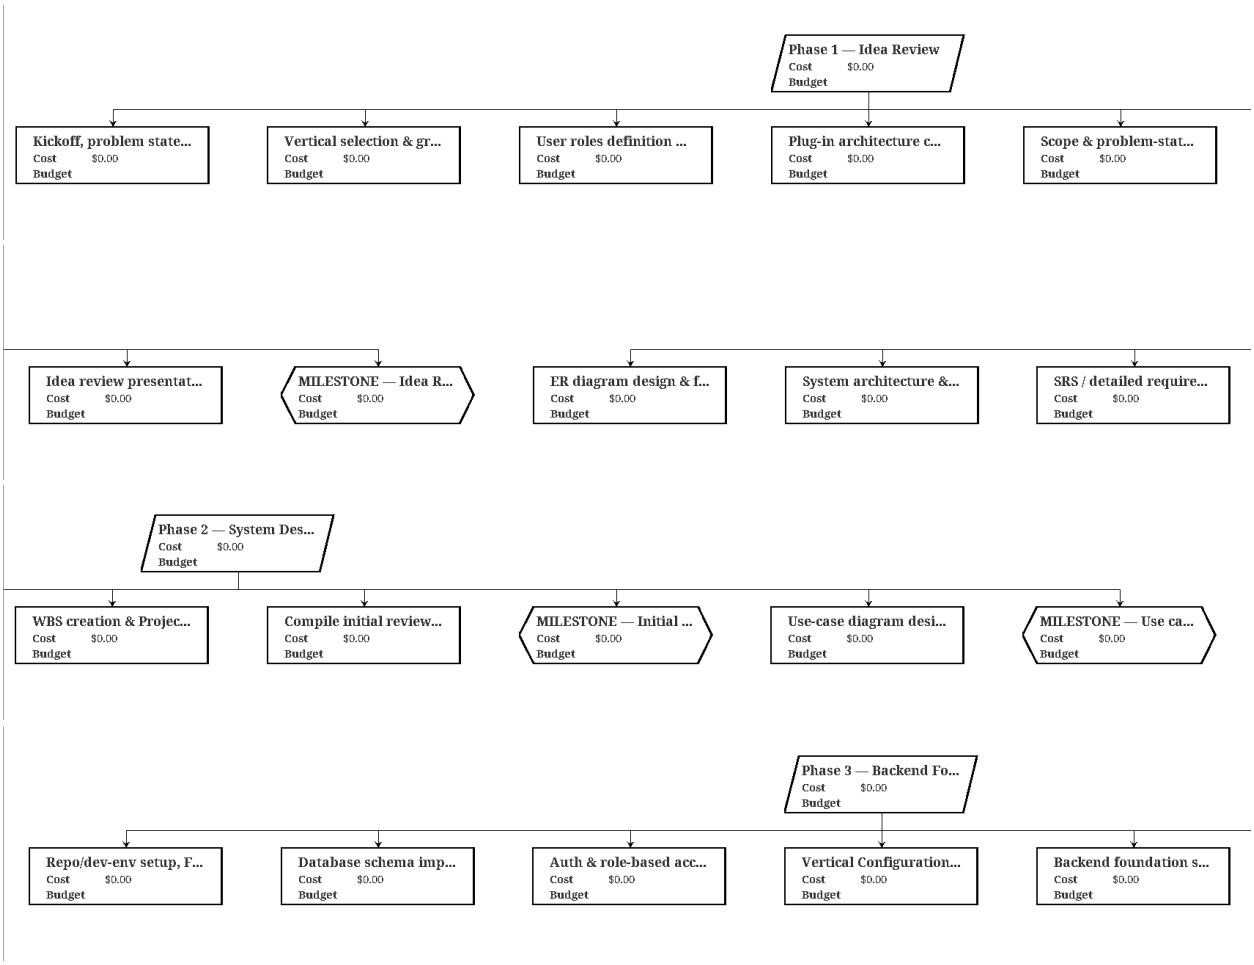
LAB 2 – Development of Work Breakdown Structure for the project after considering all the tasks involved.

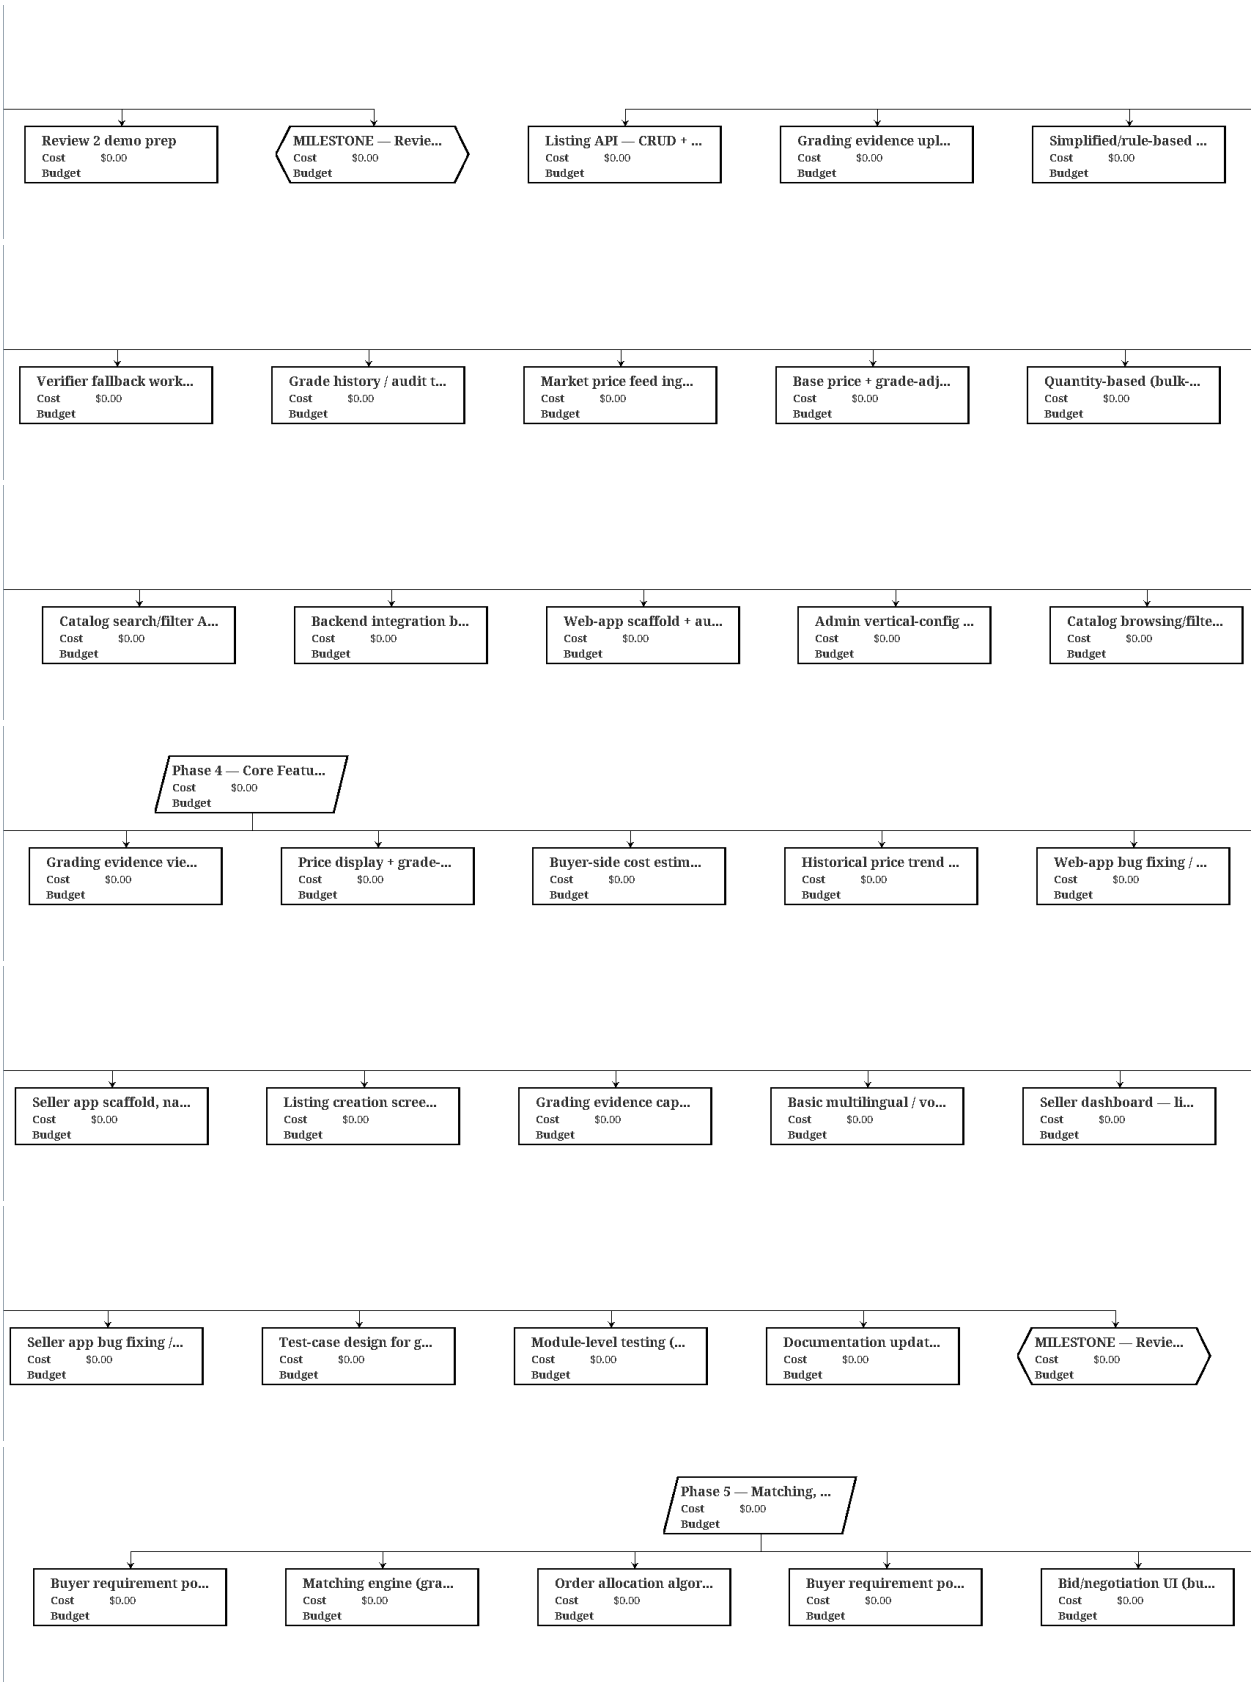
TEAM MEMBERS:

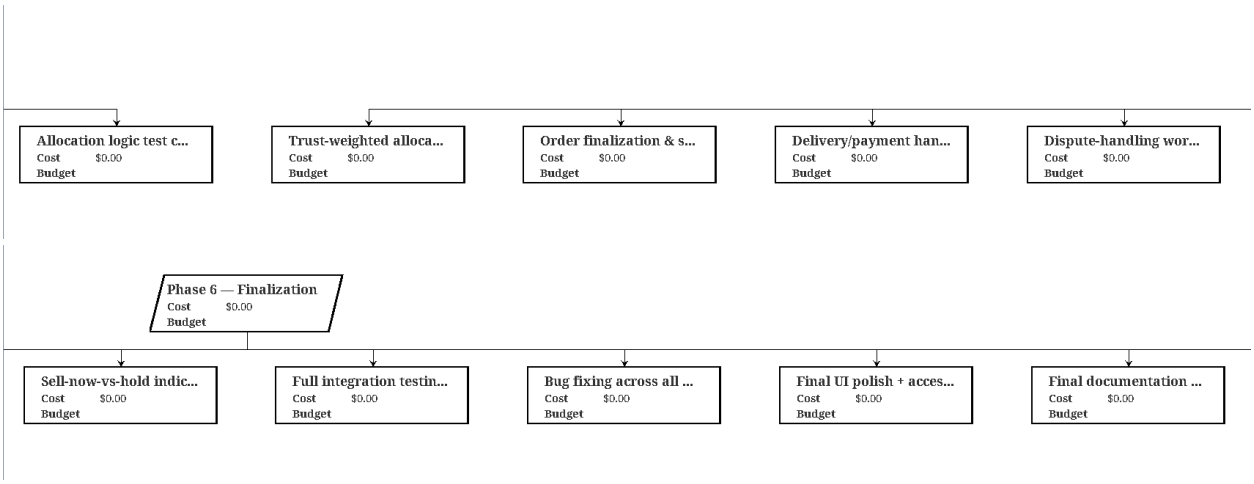
24BDS1209 – YASH RAJ

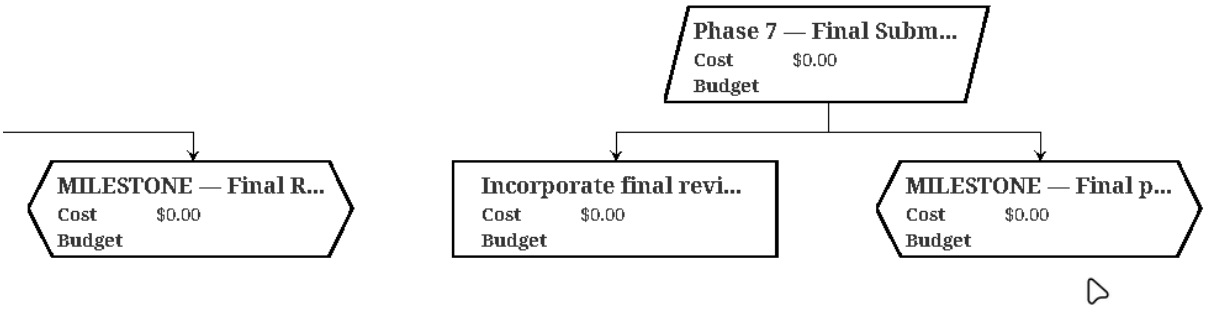
24BDS1094 – ARYAN RAJ

WORK – BREAKDOWN STRUCTURE (WBS)

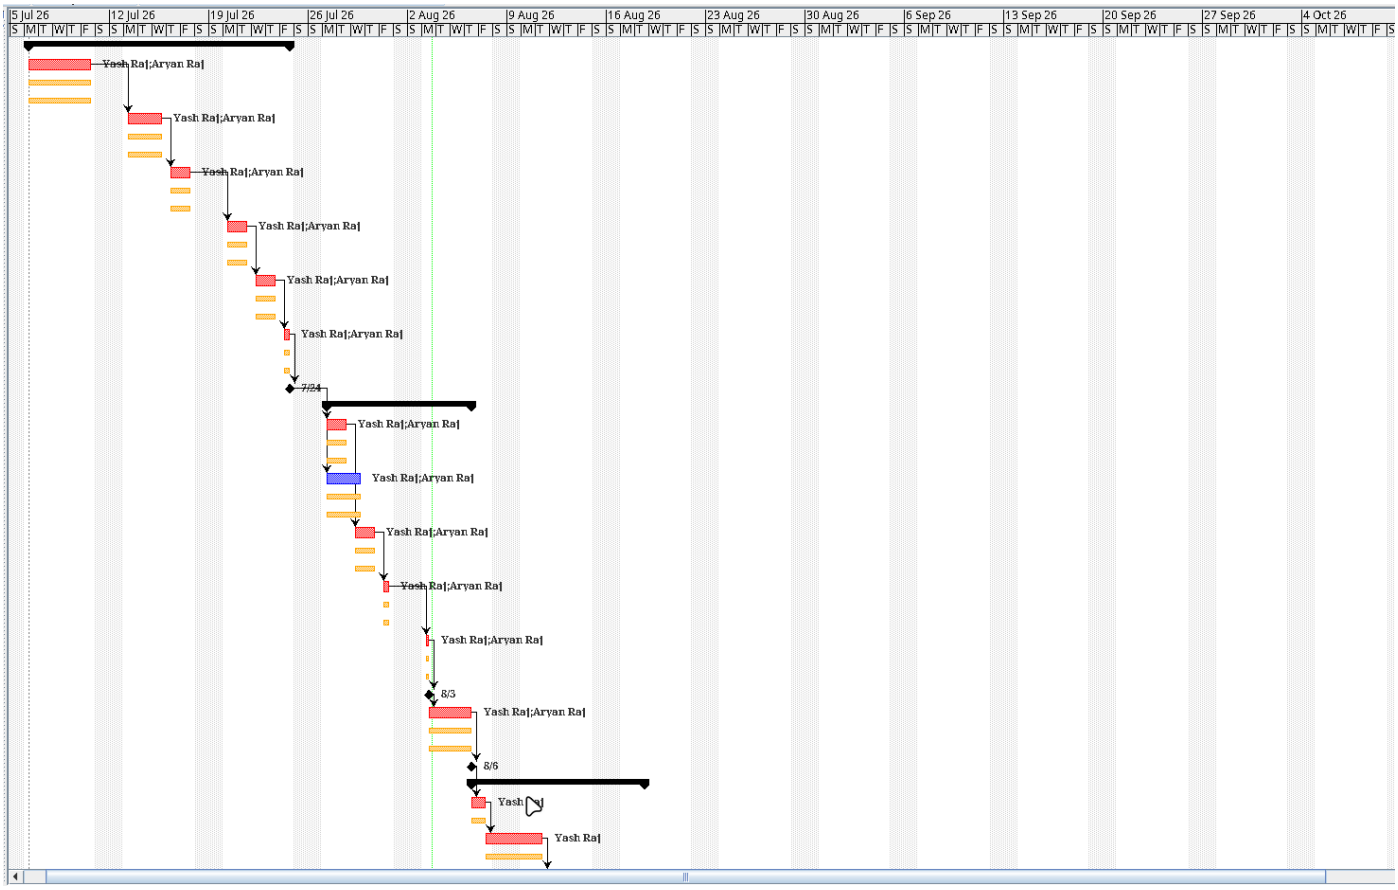


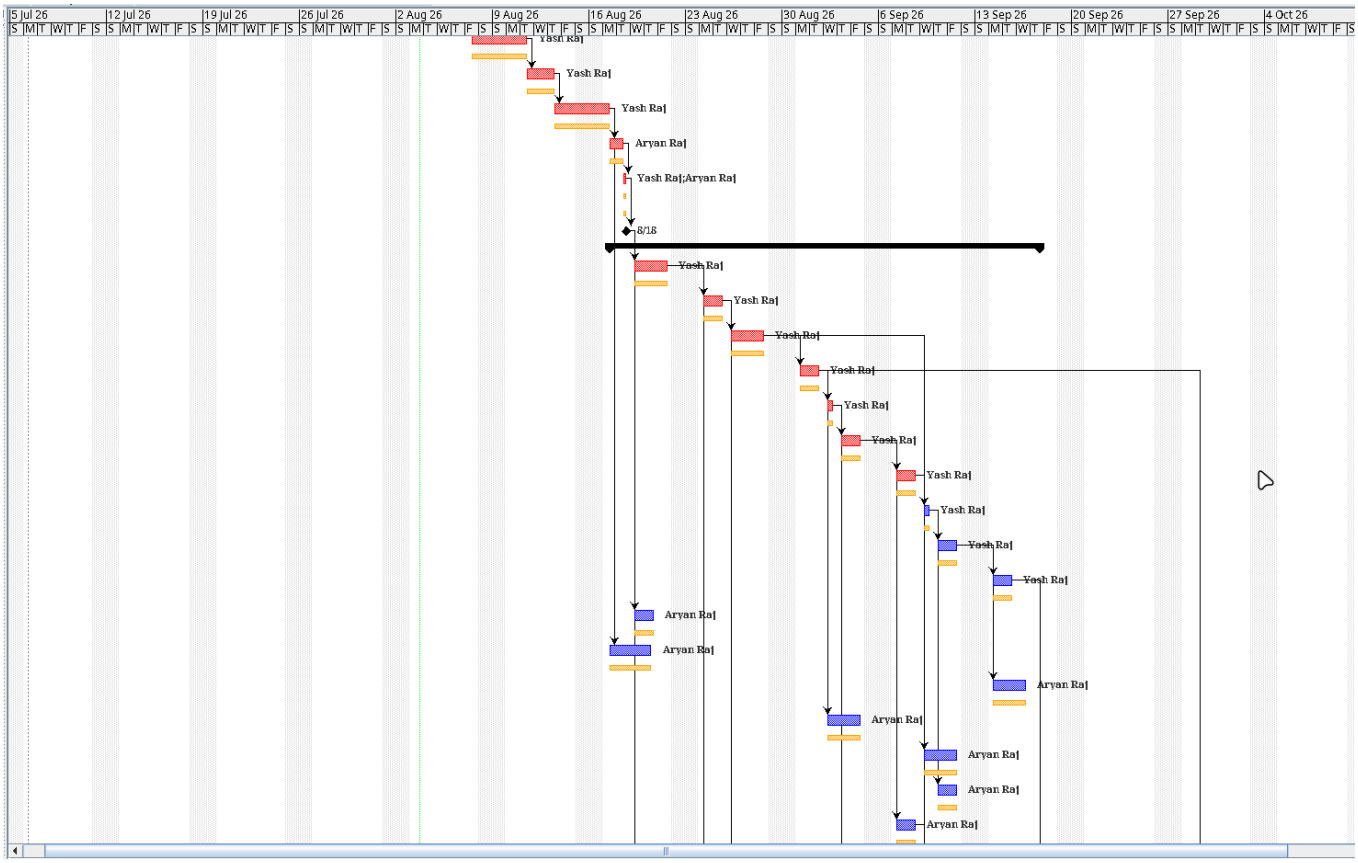

Review 2 demo prep
Cost $0.00
Budget
MILESTONE — Revie...
Cost $0.00
Budget
Listing API — CRUD + ...
Cost $0.00
Budget
Grading evidence upl...
Cost $0.00
Budget
Simplified/rule-based ...
Cost $0.00
Budget
Verifier fallback work...
Cost $0.00
Budget
Grade history / audit t...
Cost $0.00
Budget
Market price feed ing...
Cost $0.00
Budget
Base price + grade-adj...
Cost $0.00
Budget
Quantity-based (bulk-...
Cost $0.00
Budget
Catalog search/filter A...
Cost $0.00
Budget
Backend integration b...
Cost $0.00
Budget
Web-app scaffold + au...
Cost $0.00
Budget
Admin vertical-config ...
Cost $0.00
Budget
Catalog browsing/filte...
Cost $0.00
Budget
Phase 4 — Core Featu...
Cost $0.00
Budget
Grading evidence vie...
Cost $0.00
Budget
Price display + grade-...
Cost $0.00
Budget
Buyer-side cost estim...
Cost $0.00
Budget
Historical price trend ...
Cost $0.00
Budget
Web-app bug fixing / ...
Cost $0.00
Budget
Seller app scaffold, na...
Cost $0.00
Budget
Listing creation scree...
Cost $0.00
Budget
Grading evidence cap...
Cost $0.00
Budget
Basic multilingual / vo...
Cost $0.00
Budget
Seller dashboard — li...
Cost $0.00
Budget
Seller app bug fixing /...
Cost $0.00
Budget
Test-case design for g...
Cost $0.00
Budget
Module-level testing (...
Cost $0.00
Budget
Documentation updat...
Cost $0.00
Budget
MILESTONE — Revie...
Cost $0.00
Budget
Phase 5 — Matching, ...
Cost $0.00
Budget
Buyer requirement po...
Cost $0.00
Budget
Matching engine (gra...
Cost $0.00
Budget
Order allocation algor...
Cost $0.00
Budget
Buyer requirement po...
Cost $0.00
Budget
Bid/negotiation UI (bu...
Cost $0.00
Budget

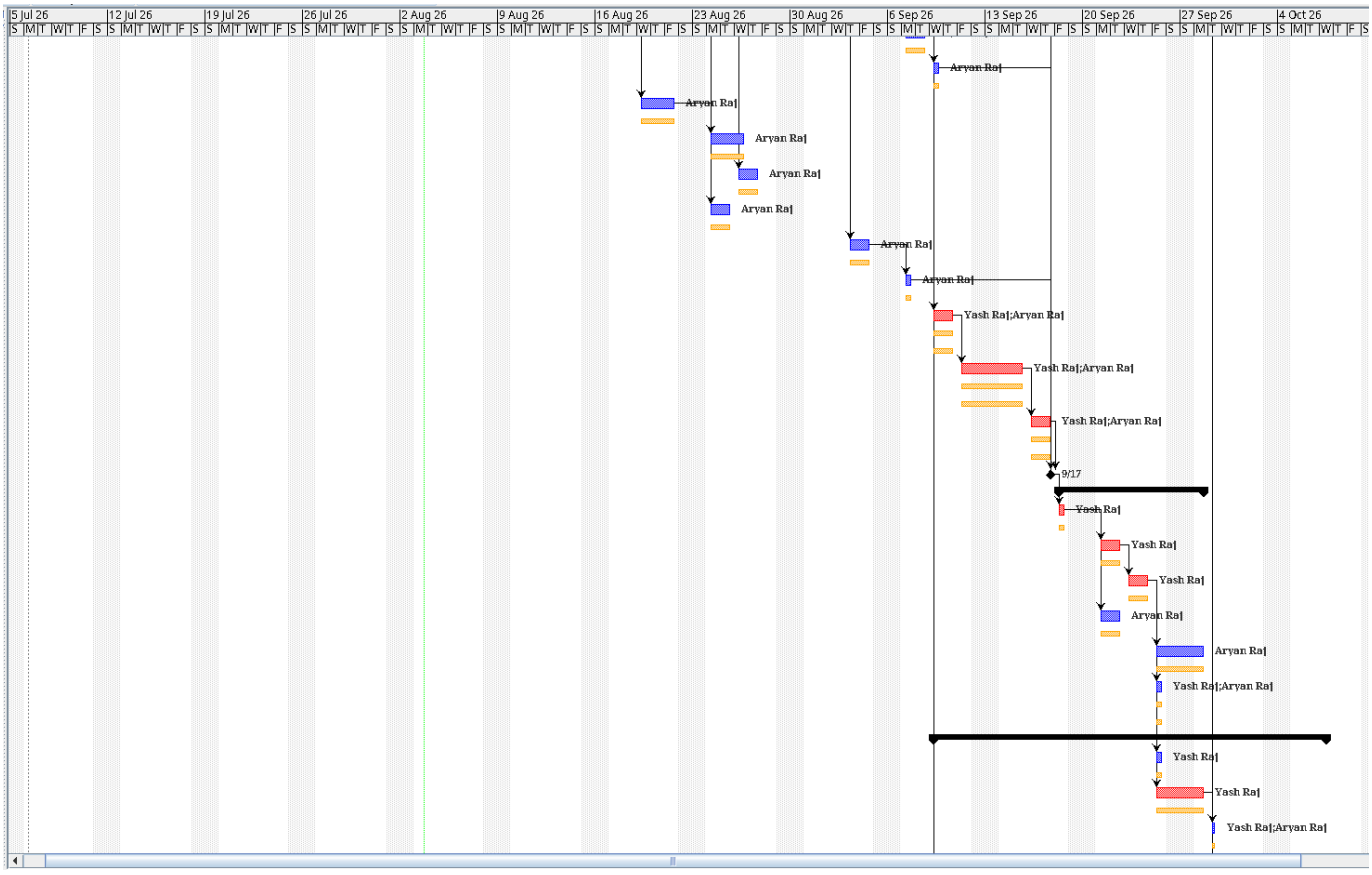

Allocation logic test c...
Cost $0.00
Budget
Trust-weighted alloca...
Cost $0.00
Budget
Order finalization & s...
Cost $0.00
Budget
Delivery/payment han...
Cost $0.00
Budget
Dispute-handling wor...
Cost $0.00
Budget
Phase 6 — Finalization
Cost $0.00
Budget
Sell-now-vs-hold indic...
Cost $0.00
Budget
Full integration testin...
Cost $0.00
Budget
Bug fixing across all ...
Cost $0.00
Budget
Final UI polish + acces...
Cost $0.00
Budget
Final documentation ...
Cost $0.00
Budget

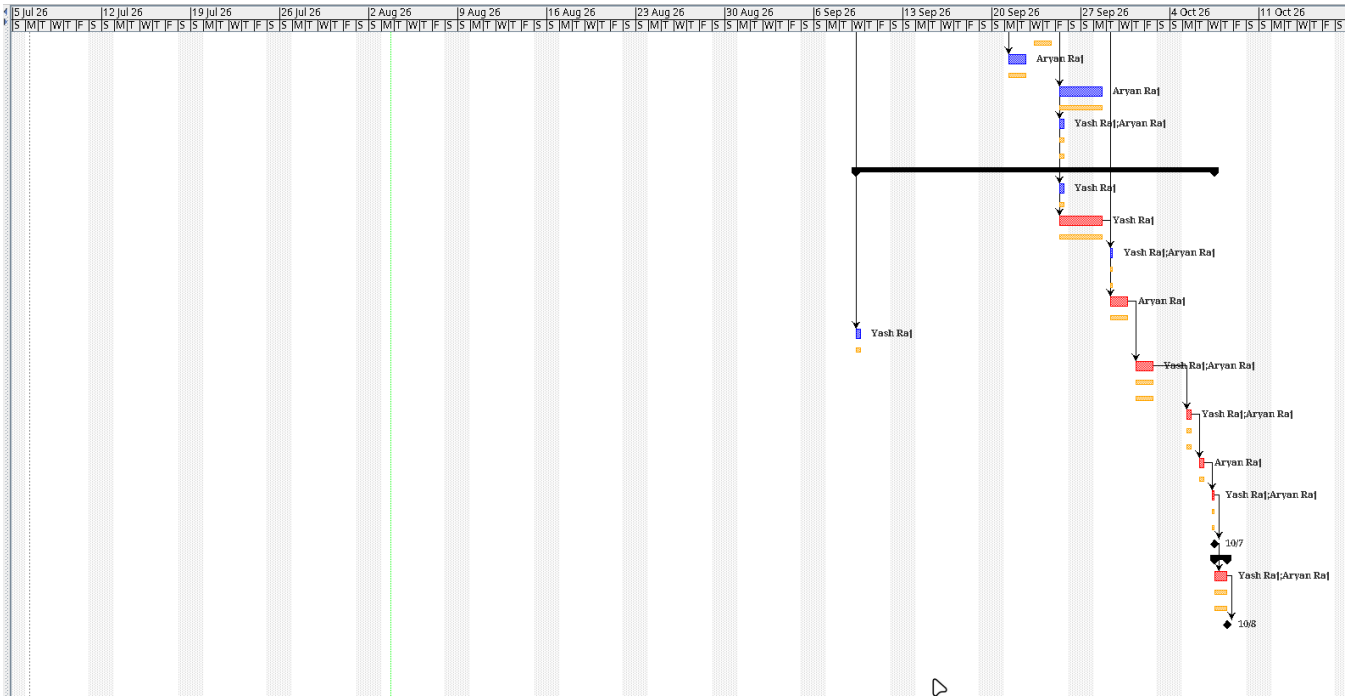

Phase 7 — Final Subm...
Cost $0.00
Budget
MILESTONE — Final R...
Cost $0.00
Budget
Incorporate final revi...
Cost $0.00
Budget
MILESTONE — Final p...
Cost $0.00
Budget

GANTT CHART:


5 Jul 26
12 Jul 26
19 Jul 26
26 Jul 26
2 Aug 26
9 Aug 26
16 Aug 26
23 Aug 26
30 Aug 26
6 Sep 26
13 Sep 26
20 Sep 26
27 Sep 26
4 Oct 26
Yash Ra;Aryan Ra
Yash Ra;Aryan Ra
Yash Ra;Aryan Ra
Yash Ra;Aryan Ra
Yash Ra;Aryan Ra
Yash Ra;Aryan Ra
7/24
Yash Ra;Aryan Ra
Yash Ra;Aryan Ra
Yash Ra;Aryan Ra
Yash Ra;Aryan Ra
Yash Ra;Aryan Ra
8/3
Yash Ra;Aryan Ra
8/6
Yash
Yash Ra


5 Jul 26
12 Jul 26
19 Jul 26
26 Jul 26
2 Aug 26
9 Aug 26
16 Aug 26
23 Aug 26
30 Aug 26
6 Sep 26
13 Sep 26
20 Sep 26
27 Sep 26
4 Oct 26
Yash Raj
Aryan Raj
Yash Raj;Aryan Raj
8/18


5 Jul 26
12 Jul 26
19 Jul 26
26 Jul 26
2 Aug 26
9 Aug 26
16 Aug 26
23 Aug 26
30 Aug 26
6 Sep 26
13 Sep 26
20 Sep 26
27 Sep 26
4 Oct 26
Aryan Raj
Yash Raj;Aryan Raj
9/17
Yash Raj
Yash Raj
Yash Raj
Aryan Raj
Yash Raj;Aryan Raj
Yash Raj


5 Jul 26
12 Jul 26
19 Jul 26
26 Jul 26
2 Aug 26
9 Aug 26
16 Aug 26
23 Aug 26
30 Aug 26
6 Sep 26
13 Sep 26
20 Sep 26
27 Sep 26
4 Oct 26
11 Oct 26
Aryan Raj
Aryan Raj
Yash Raj;Aryan Raj
Yash Raj
Yash Raj
Yash Raj;Aryan Raj
Aryan Raj
Yash Raj
Yash Raj;Aryan Raj
Yash Raj;Aryan Raj
Aryan Raj
Yash Raj;Aryan Raj
10/7
Yash Raj;Aryan Raj
10/8

FINAL PLAN:

		Name	Duration	Start	Finish	Predecessors	Resource Names
1		**Phase 1 — Idea Review**	**15 days**	**7/6/26, 8:00 AM**	**7/24/26, 5:00 PM**		
2		Kickoff, problem statement & MSME domain research	5 days	7/6/26, 8:00 AM	7/10/26, 5:00 PM		Yash Raj;Aryan Raj
		Aryan Raj	*5 days*	*7/6/26, 8:00 AM*	*7/10/26, 5:00 PM*		
		Yash Raj	*5 days*	*7/6/26, 8:00 AM*	*7/10/26, 5:00 PM*		
3		Vertical selection & grading-attribute study (8 sectors)	3 days	7/13/26, 8:00 AM	7/15/26, 5:00 PM	2	Yash Raj;Aryan Raj
		Aryan Raj	*3 days*	*7/13/26, 8:00 AM*	*7/15/26, 5:00 PM*		
		Yash Raj	*3 days*	*7/13/26, 8:00 AM*	*7/15/26, 5:00 PM*		
4		User roles definition & feature list drafting	2 days	7/16/26, 8:00 AM	7/17/26, 5:00 PM	3	Yash Raj;Aryan Raj
		Aryan Raj	*2 days*	*7/16/26, 8:00 AM*	*7/17/26, 5:00 PM*		
		Yash Raj	*2 days*	*7/16/26, 8:00 AM*	*7/17/26, 5:00 PM*		
5		Plug-in architecture concept (generic engine + config model)	2 days	7/20/26, 8:00 AM	7/21/26, 5:00 PM	4	Yash Raj;Aryan Raj
		Aryan Raj	*2 days*	*7/20/26, 8:00 AM*	*7/21/26, 5:00 PM*		
		Yash Raj	*2 days*	*7/20/26, 8:00 AM*	*7/21/26, 5:00 PM*		
6		Scope & problem-statement finalization	2 days	7/22/26, 8:00 AM	7/23/26, 5:00 PM	5	Yash Raj;Aryan Raj
		Aryan Raj	*2 days*	*7/22/26, 8:00 AM*	*7/23/26, 5:00 PM*		
		Yash Raj	*2 days*	*7/22/26, 8:00 AM*	*7/23/26, 5:00 PM*		
7		Idea review presentation prep	1 day	7/24/26, 8:00 AM	7/24/26, 5:00 PM	6	Yash Raj;Aryan Raj
		Aryan Raj	*1 day*	*7/24/26, 8:00 AM*	*7/24/26, 5:00 PM*		
		Yash Raj	*1 day*	*7/24/26, 8:00 AM*	*7/24/26, 5:00 PM*		
8		MILESTONE — Idea Review	0 days	7/24/26, 5:00 PM	7/24/26, 5:00 PM	7	
9		**Phase 2 — System Design & Documentation**	**8.5 days**	**7/27/26, 8:00 AM**	**8/6/26, 1:00 PM**		
10		ER diagram design & finalization (all entities + relations)	2 days	7/27/26, 8:00 AM	7/28/26, 5:00 PM	8	Yash Raj;Aryan Raj
		Aryan Raj	*2 days*	*7/27/26, 8:00 AM*	*7/28/26, 5:00 PM*		
		Yash Raj	*2 days*	*7/27/26, 8:00 AM*	*7/28/26, 5:00 PM*		
11		System architecture & tech-stack decisions	3 days	7/27/26, 8:00 AM	7/29/26, 5:00 PM	8	Yash Raj;Aryan Raj
		Aryan Raj	*3 days*	*7/27/26, 8:00 AM*	*7/29/26, 5:00 PM*		
		Yash Raj	*3 days*	*7/27/26, 8:00 AM*	*7/29/26, 5:00 PM*		
12		SRS / detailed requirements document	2 days	7/29/26, 8:00 AM	7/30/26, 5:00 PM	10	Yash Raj;Aryan Raj
		Aryan Raj	*2 days*	*7/29/26, 8:00 AM*	*7/30/26, 5:00 PM*		
		Yash Raj	*2 days*	*7/29/26, 8:00 AM*	*7/30/26, 5:00 PM*		
13		WBS creation & ProjectLibre schedule setup	1 day	7/31/26, 8:00 AM	7/31/26, 5:00 PM	12	Yash Raj;Aryan Raj
		Aryan Raj	*1 day*	*7/31/26, 8:00 AM*	*7/31/26, 5:00 PM*		
		Yash Raj	*1 day*	*7/31/26, 8:00 AM*	*7/31/26, 5:00 PM*		
14		Compile initial review package	0.5 days	8/3/26, 8:00 AM	8/3/26, 1:00 PM	13	Yash Raj;Aryan Raj
		Aryan Raj	*0.5 days*	*8/3/26, 8:00 AM*	*8/3/26, 1:00 PM*		
		Yash Raj	*0.5 days*	*8/3/26, 8:00 AM*	*8/3/26, 1:00 PM*		
15		MILESTONE — Initial review docs submitted (ER, WBS, SRS)	0 days	8/3/26, 1:00 PM	8/3/26, 1:00 PM	14	
16		Use-case diagram design in StarUML (all roles × features)	3 days	8/3/26, 1:00 PM	8/6/26, 1:00 PM	15	Yash Raj;Aryan Raj
		Aryan Raj	*3 days*	*8/3/26, 1:00 PM*	*8/6/26, 1:00 PM*		
		Yash Raj	*3 days*	*8/3/26, 1:00 PM*	*8/6/26, 1:00 PM*		
17		MILESTONE — Use case diagram submitted	0 days	8/6/26, 1:00 PM	8/6/26, 1:00 PM	16	
18		**Phase 3 — Backend Foundation**	**3.5 days**	**8/6/26, 1:00 PM**	**8/18/26, 5:00 PM**		
19		Repo/dev-env setup, FastAPI skeleton, PostgreSQL provisioning	1 day	8/6/26, 1:00 PM	8/7/26, 1:00 PM	17	Yash Raj
		Yash Raj	*1 day*	*8/6/26, 1:00 PM*	*8/7/26, 1:00 PM*		
20		Database schema implementation from ER diagram (all tables)	2 days	8/7/26, 1:00 PM	8/11/26, 1:00 PM	19	Yash Raj
		Yash Raj	*2 days*	*8/7/26, 1:00 PM*	*8/11/26, 1:00 PM*		

		Name	Duration	Start	Finish	Predecessors	Resource Names
21		Auth & role-based access control (Seller/Buyer/Admin/Verifier)	2 days	8/11/26, 1:00 PM	8/13/26, 1:00 PM	20	Yash Raj
		Yash Raj	*2 days*	*8/11/26, 1:00 PM*	*8/13/26, 1:00 PM*		
22		Vertical Configuration module — admin CRUD for grading_schema & price_rules	2 days	8/13/26, 1:00 PM	8/17/26, 1:00 PM	21	Yash Raj
		Yash Raj	*2 days*	*8/13/26, 1:00 PM*	*8/17/26, 1:00 PM*		
23		Backend foundation smoke test	1 day	8/17/26, 1:00 PM	8/18/26, 1:00 PM	22	Aryan Raj
		Aryan Raj	*1 day*	*8/17/26, 1:00 PM*	*8/18/26, 1:00 PM*		
24		Review 2 demo prep	0.5 days	8/18/26, 1:00 PM	8/18/26, 5:00 PM	23	Yash Raj;Aryan Raj
		Aryan Raj	*0.5 days*	*8/18/26, 1:00 PM*	*8/18/26, 5:00 PM*		
		Yash Raj	*0.5 days*	*8/18/26, 1:00 PM*	*8/18/26, 5:00 PM*		
25		MILESTONE — Review 2	0 days	8/18/26, 5:00 PM	8/18/26, 5:00 PM	24	
26		**⊟Phase 4 — Core Feature Development**	**23.5 days**	**8/17/26, 1:00 PM**	**9/17/26, 5:00 PM**		
27		Listing API — CRUD + offline queue/sync support	3 days	8/19/26, 8:00 AM	8/21/26, 5:00 PM	25	Yash Raj
		Yash Raj	*3 days*	*8/19/26, 8:00 AM*	*8/21/26, 5:00 PM*		
28		Grading evidence upload API (photo/video/doc storage)	2 days	8/24/26, 8:00 AM	8/25/26, 5:00 PM	27	Yash Raj
		Yash Raj	*2 days*	*8/24/26, 8:00 AM*	*8/25/26, 5:00 PM*		
29		Simplified/rule-based grading scorer + confidence score	3 days	8/26/26, 8:00 AM	8/28/26, 5:00 PM	28	Yash Raj
		Yash Raj	*3 days*	*8/26/26, 8:00 AM*	*8/28/26, 5:00 PM*		
30		Verifier fallback workflow API (flag → review → confirm/override)	2 days	8/31/26, 8:00 AM	9/1/26, 5:00 PM	29	Yash Raj
		Yash Raj	*2 days*	*8/31/26, 8:00 AM*	*9/1/26, 5:00 PM*		
31		Grade history / audit trail logging	1 day	9/2/26, 8:00 AM	9/2/26, 5:00 PM	30	Yash Raj
		Yash Raj	*1 day*	*9/2/26, 8:00 AM*	*9/2/26, 5:00 PM*		
32		Market price feed ingestion (seed/mock data per vertical)	2 days	9/3/26, 8:00 AM	9/4/26, 5:00 PM	31	Yash Raj
		Yash Raj	*2 days*	*9/3/26, 8:00 AM*	*9/4/26, 5:00 PM*		
33		Base price + grade-adjusted price calculator API	2 days	9/7/26, 8:00 AM	9/8/26, 5:00 PM	32	Yash Raj
		Yash Raj	*2 days*	*9/7/26, 8:00 AM*	*9/8/26, 5:00 PM*		
34		Quantity-based (bulk-tiered) price calculator API	1 day	9/9/26, 8:00 AM	9/9/26, 5:00 PM	33	Yash Raj
		Yash Raj	*1 day*	*9/9/26, 8:00 AM*	*9/9/26, 5:00 PM*		
35		Catalog search/filter API	2 days	9/10/26, 8:00 AM	9/11/26, 5:00 PM	34	Yash Raj
		Yash Raj	*2 days*	*9/10/26, 8:00 AM*	*9/11/26, 5:00 PM*		
36		Backend integration buffer / bug-fix	2 days	9/14/26, 8:00 AM	9/15/26, 5:00 PM	35	Yash Raj
		Yash Raj	*2 days*	*9/14/26, 8:00 AM*	*9/15/26, 5:00 PM*		
37		Web-app scaffold + auth screens	2 days	8/19/26, 8:00 AM	8/20/26, 5:00 PM	25	Aryan Raj
		Aryan Raj	*2 days*	*8/19/26, 8:00 AM*	*8/20/26, 5:00 PM*		
38		Admin vertical-config UI	3 days	8/17/26, 1:00 PM	8/20/26, 1:00 PM	22	Aryan Raj
		Aryan Raj	*3 days*	*8/17/26, 1:00 PM*	*8/20/26, 1:00 PM*		
39		Catalog browsing/filtering UI	3 days	9/14/26, 8:00 AM	9/16/26, 5:00 PM	35	Aryan Raj
		Aryan Raj	*3 days*	*9/14/26, 8:00 AM*	*9/16/26, 5:00 PM*		
40		Grading evidence viewer + verifier review UI	3 days	9/2/26, 8:00 AM	9/4/26, 5:00 PM	30	Aryan Raj
		Aryan Raj	*3 days*	*9/2/26, 8:00 AM*	*9/4/26, 5:00 PM*		
41		Price display + grade-adjusted price UI	3 days	9/9/26, 8:00 AM	9/11/26, 5:00 PM	33	Aryan Raj
		Aryan Raj	*3 days*	*9/9/26, 8:00 AM*	*9/11/26, 5:00 PM*		
42		Buyer-side cost estimator UI	2 days	9/10/26, 8:00 AM	9/11/26, 5:00 PM	34	Aryan Raj
		Aryan Raj	*2 days*	*9/10/26, 8:00 AM*	*9/11/26, 5:00 PM*		
43		Historical price trend chart UI	2 days	9/7/26, 8:00 AM	9/8/26, 5:00 PM	32	Aryan Raj
		Aryan Raj	*2 days*	*9/7/26, 8:00 AM*	*9/8/26, 5:00 PM*		
44		Web-app bug fixing / polish	1 day	9/9/26, 8:00 AM	9/9/26, 5:00 PM	43	Aryan Raj
		Aryan Raj	*1 day*	*9/9/26, 8:00 AM*	*9/9/26, 5:00 PM*		

		Name	Duration	Start	Finish	Predecessors	Resource Names
		Aryan Raj	*3 days*	*8/19/26, 8:00 AM*	*8/21/26, 5:00 PM*		
46		Listing creation screens (offline-tolerant, sync queue)	3 days	8/24/26, 8:00 AM	8/26/26, 5:00 PM	27	Aryan Raj
		Aryan Raj	*3 days*	*8/24/26, 8:00 AM*	*8/26/26, 5:00 PM*		
47		Grading evidence capture (camera/file upload) screens	2 days	8/26/26, 8:00 AM	8/27/26, 5:00 PM	28	Aryan Raj
		Aryan Raj	*2 days*	*8/26/26, 8:00 AM*	*8/27/26, 5:00 PM*		
48		Basic multilingual / voice-assisted input layer (stretch)	2 days	8/24/26, 8:00 AM	8/25/26, 5:00 PM	45	Aryan Raj
		Aryan Raj	*2 days*	*8/24/26, 8:00 AM*	*8/25/26, 5:00 PM*		
49		Seller dashboard — listing status & grade-history view	2 days	9/3/26, 8:00 AM	9/4/26, 5:00 PM	31	Aryan Raj
		Aryan Raj	*2 days*	*9/3/26, 8:00 AM*	*9/4/26, 5:00 PM*		
50		Seller app bug fixing / polish	1 day	9/7/26, 8:00 AM	9/7/26, 5:00 PM	49	Aryan Raj
		Aryan Raj	*1 day*	*9/7/26, 8:00 AM*	*9/7/26, 5:00 PM*		
51		Test-case design for grading & pricing modules	2 days	9/9/26, 8:00 AM	9/10/26, 5:00 PM	29;33	Yash Raj;Aryan Raj
		Aryan Raj	*2 days*	*9/9/26, 8:00 AM*	*9/10/26, 5:00 PM*		
		Yash Raj	*2 days*	*9/9/26, 8:00 AM*	*9/10/26, 5:00 PM*		
52		Module-level testing (backend + web + mobile)	3 days	9/11/26, 8:00 AM	9/15/26, 5:00 PM	51	Yash Raj;Aryan Raj
		Aryan Raj	*3 days*	*9/11/26, 8:00 AM*	*9/15/26, 5:00 PM*		
		Yash Raj	*3 days*	*9/11/26, 8:00 AM*	*9/15/26, 5:00 PM*		
53		Documentation update (user manual draft, API docs)	2 days	9/16/26, 8:00 AM	9/17/26, 5:00 PM	52	Yash Raj;Aryan Raj
		Yash Raj	*2 days*	*9/16/26, 8:00 AM*	*9/17/26, 5:00 PM*		
		Aryan Raj	*2 days*	*9/16/26, 8:00 AM*	*9/17/26, 5:00 PM*		
54		MILESTONE — Review 3 (demo grading + pricing across all apps)	0 days	9/17/26, 5:00 PM	9/17/26, 5:00 PM	36;44;50;53	
55		**⊟Phase 5 — Matching, Allocation & Trust**	**5 days**	**9/18/26, 8:00 AM**	**9/28/26, 5:00 PM**		
56		Buyer requirement posting API	1 day	9/18/26, 8:00 AM	9/18/26, 5:00 PM	54	Yash Raj
		Yash Raj	*1 day*	*9/18/26, 8:00 AM*	*9/18/26, 5:00 PM*		
57		Matching engine (grade / qty / region filter logic)	2 days	9/21/26, 8:00 AM	9/22/26, 5:00 PM	56	Yash Raj
		Yash Raj	*2 days*	*9/21/26, 8:00 AM*	*9/22/26, 5:00 PM*		
58		Order allocation algorithm across multiple sellers	2 days	9/23/26, 8:00 AM	9/24/26, 5:00 PM	57	Yash Raj
		Yash Raj	*2 days*	*9/23/26, 8:00 AM*	*9/24/26, 5:00 PM*		
59		Buyer requirement posting UI + cost estimator hookup	2 days	9/21/26, 8:00 AM	9/22/26, 5:00 PM	56	Aryan Raj
		Aryan Raj	*2 days*	*9/21/26, 8:00 AM*	*9/22/26, 5:00 PM*		
60		Bid/negotiation UI (buyer & seller side)	2 days	9/25/26, 8:00 AM	9/28/26, 5:00 PM	58	Aryan Raj
		Aryan Raj	*2 days*	*9/25/26, 8:00 AM*	*9/28/26, 5:00 PM*		
61		Allocation logic test cases (multi-seller scenarios)	1 day	9/25/26, 8:00 AM	9/25/26, 5:00 PM	58	Yash Raj;Aryan Raj
		Aryan Raj	*1 day*	*9/25/26, 8:00 AM*	*9/25/26, 5:00 PM*		
		Yash Raj	*1 day*	*9/25/26, 8:00 AM*	*9/25/26, 5:00 PM*		
62		**⊟Phase 6 — Finalization**	**15.5 days**	**9/9/26, 8:00 AM**	**10/7/26, 1:00 PM**		
63		Trust-weighted allocation + reputation scoring	1 day	9/25/26, 8:00 AM	9/25/26, 5:00 PM	58	Yash Raj
		Yash Raj	*1 day*	*9/25/26, 8:00 AM*	*9/25/26, 5:00 PM*		
64		Order finalization & status-tracking state machine	2 days	9/25/26, 8:00 AM	9/28/26, 5:00 PM	58	Yash Raj
		Yash Raj	*2 days*	*9/25/26, 8:00 AM*	*9/28/26, 5:00 PM*		
65		Delivery/payment handoff — interface stub only	0.5 days	9/29/26, 8:00 AM	9/29/26, 1:00 PM	64	Yash Raj;Aryan Raj
		Yash Raj	*0.5 days*	*9/29/26, 8:00 AM*	*9/29/26, 1:00 PM*		
		Aryan Raj	*0.5 days*	*9/29/26, 8:00 AM*	*9/29/26, 1:00 PM*		
66		Dispute-handling workflow + verification-queue UI	2 days	9/29/26, 8:00 AM	9/30/26, 5:00 PM	30;64	Aryan Raj
		Aryan Raj	*2 days*	*9/29/26, 8:00 AM*	*9/30/26, 5:00 PM*		
67		Sell-now-vs-hold indicator (stretch)	1 day	9/9/26, 8:00 AM	9/9/26, 5:00 PM	43	Yash Raj

		Name	Duration	Start	Finish	Predecessors	Resource Names
		Aryan Raj	*2 days*	*9/29/26, 8:00 AM*	*9/30/26, 5:00 PM*		
67		Sell-now-vs-hold indicator (stretch)	1 day	9/9/26, 8:00 AM	9/9/26, 5:00 PM	43	Yash Raj
		Yash Raj	*1 day*	*9/9/26, 8:00 AM*	*9/9/26, 5:00 PM*		
68		Full integration testing — end to end	2 days	10/1/26, 8:00 AM	10/2/26, 5:00 PM	66	Yash Raj;Aryan Raj
		Yash Raj	*2 days*	*10/1/26, 8:00 AM*	*10/2/26, 5:00 PM*		
		Aryan Raj	*2 days*	*10/1/26, 8:00 AM*	*10/2/26, 5:00 PM*		
69		Bug fixing across all modules	1 day	10/5/26, 8:00 AM	10/5/26, 5:00 PM	68	Yash Raj;Aryan Raj
		Aryan Raj	*1 day*	*10/5/26, 8:00 AM*	*10/5/26, 5:00 PM*		
		Yash Raj	*1 day*	*10/5/26, 8:00 AM*	*10/5/26, 5:00 PM*		
70		Final UI polish + accessibility pass	1 day	10/6/26, 8:00 AM	10/6/26, 5:00 PM	69	Aryan Raj
		Aryan Raj	*1 day*	*10/6/26, 8:00 AM*	*10/6/26, 5:00 PM*		
71		Final documentation & presentation prep	0.5 days	10/7/26, 8:00 AM	10/7/26, 1:00 PM	70	Yash Raj;Aryan Raj
		Aryan Raj	*0.5 days*	*10/7/26, 8:00 AM*	*10/7/26, 1:00 PM*		
		Yash Raj	*0.5 days*	*10/7/26, 8:00 AM*	*10/7/26, 1:00 PM*		
72		MILESTONE — Final Review	0 days	10/7/26, 1:00 PM	10/7/26, 1:00 PM	71	
73		**⊟Phase 7 — Final Submission**	**1 day**	**10/7/26, 1:00 PM**	**10/8/26, 1:00 PM**		
74		Incorporate final review feedback	1 day	10/7/26, 1:00 PM	10/8/26, 1:00 PM	72	Yash Raj;Aryan Raj
		Aryan Raj	*1 day*	*10/7/26, 1:00 PM*	*10/8/26, 1:00 PM*		
		Yash Raj	*1 day*	*10/7/26, 1:00 PM*	*10/8/26, 1:00 PM*		
75		MILESTONE — Final project submission	0 days	10/8/26, 1:00 PM	10/8/26, 1:00 PM	74	
